

04 July 2024




# 30 Minute MTU Project Update

Member Meeting



# Housekeeping Rules

- Please keep your video switched off
- Raise your hand if you have a question
- When asked to unmute your line



*Thank you for your cooperation.*



# Agenda

- Project Update
- Market Trial
- Q&A




# Project Update

## Go-Live Date

- New go-live date of **18<sup>th</sup> March 2025** (for TD 19<sup>th</sup> March 2025)
- Delay in go-live date is due to impact from other SDAC projects (ie. Pan-European IDA's)
- There is a dependency on the go-live sequence in SIDC and SDAC
  - Local 15 min ISP → 15 min ID (Continuous + IDA) → 15 min Day-Ahead Market

# Project Update

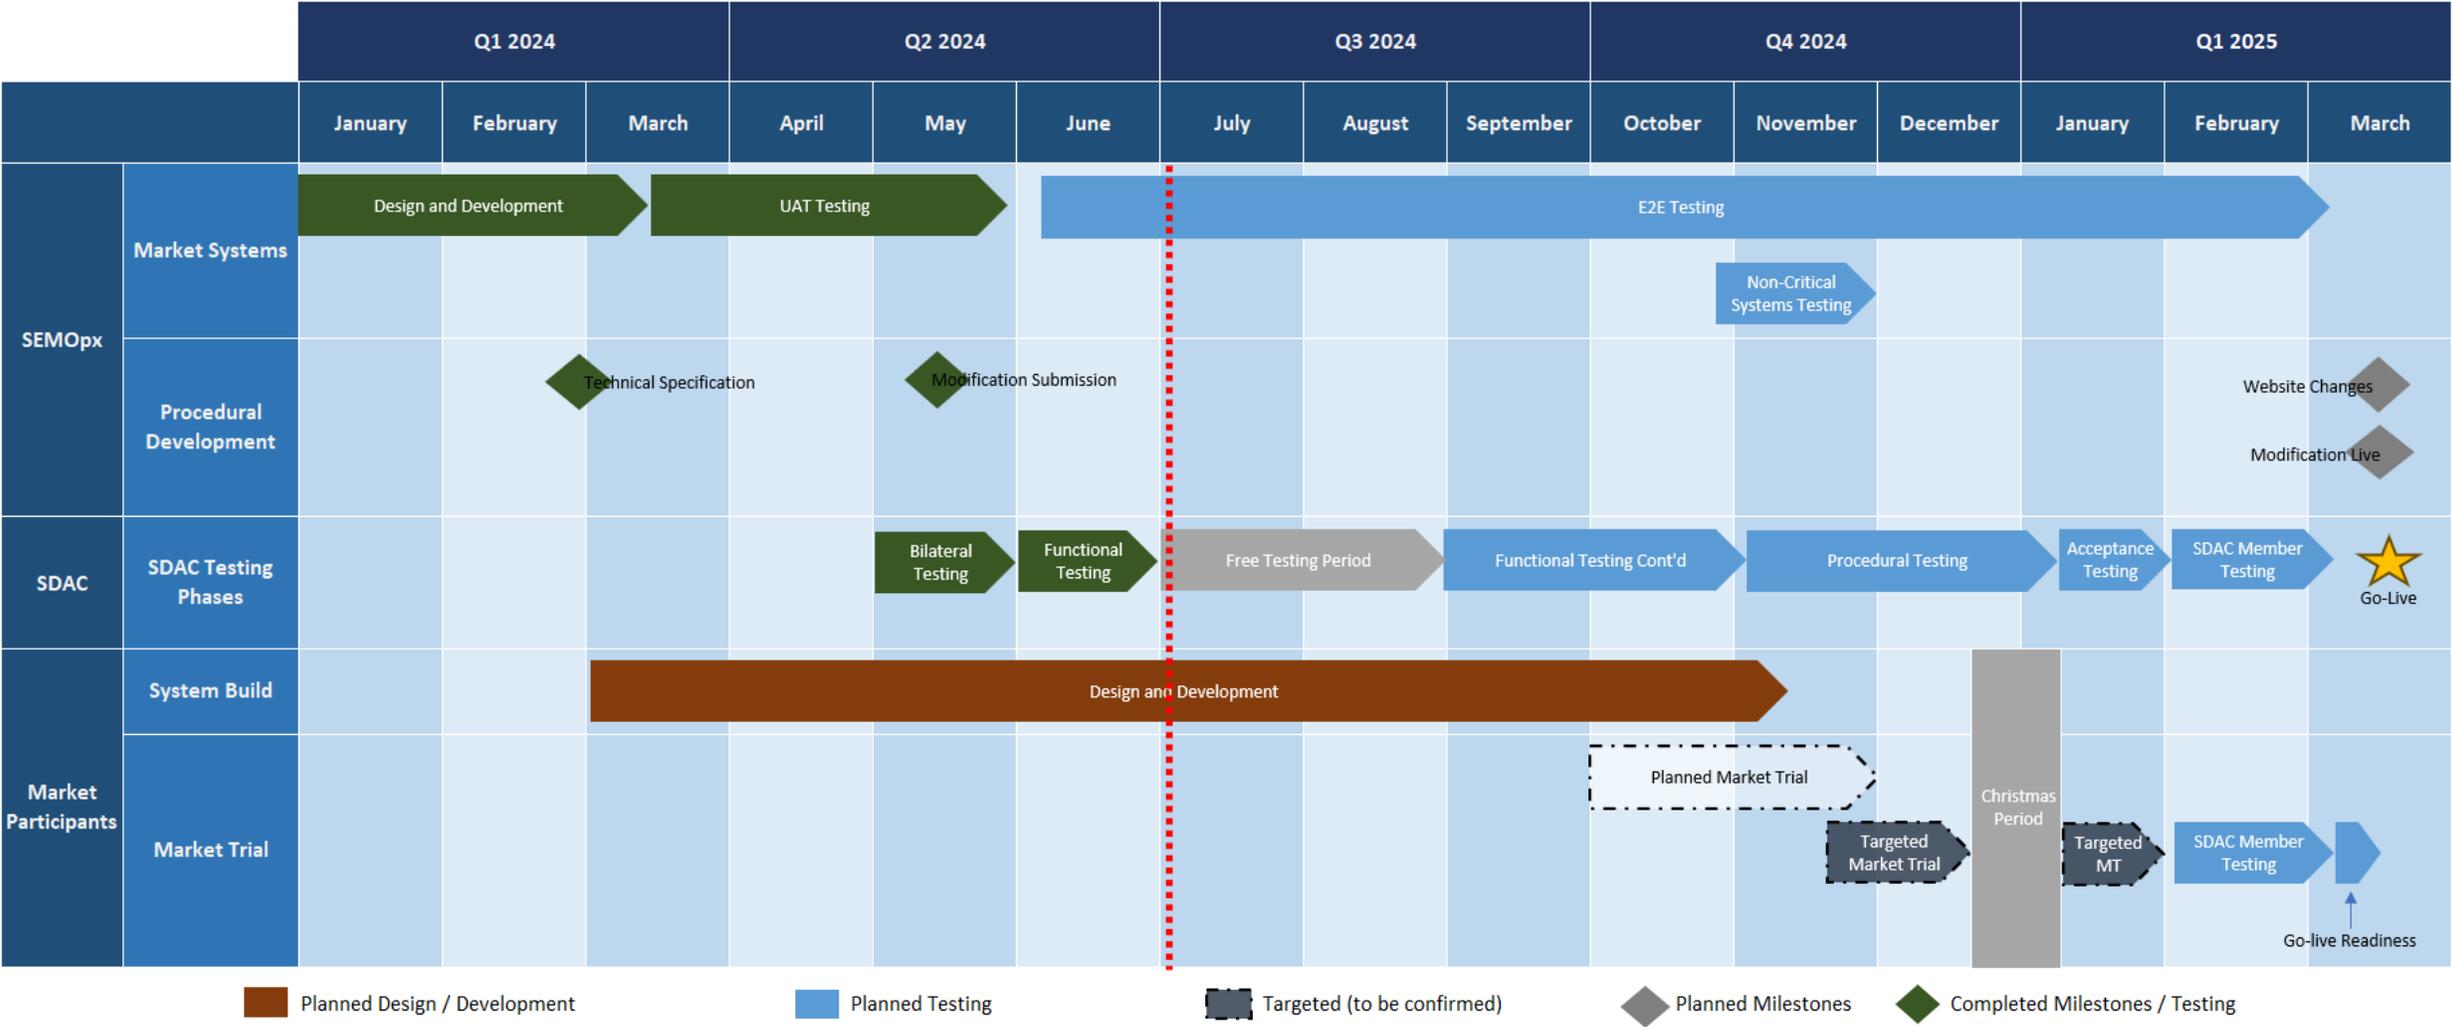

Planned Design / Development

Planned Testing

Targeted (to be confirmed)

Planned Milestones

Completed Milestones / Testing

# Project Update

## API Package and WSDL

- 15 & 30 Minute MTU application development is on-going
- SEMOpx will provide publication date for API Package and WSDL by end of August 2024

## SDAC Rollback Plan

- The rollback will be a switch back to a 60-minute configuration, to the systems and product specifications as they were the day before the declaration of rollback
- SDAC TSOs and NEMOs are working on SDAC rollback plan and a set of corrective measures to be deployed in case 15/30 min MTU go-live encounters issues
- Extensive integration testing in SDAC to reduce the risk of rollback being triggered
- Main Scenarios that could cause rollback:
  - PMB Performance Challenges
  - Significant Changes in Market Participant Behaviour
- Will affect Market Participant systems if rollback is triggered

# Market Trial & SDAC Member Testing

## Local Market Trial

- System testing of bids/order submissions and retrieval of market/trade results
- Timeline of Market Trial is dependent on the application development:
  - Planned Market Trial in Oct - Nov 2024 delayed
  - Potentially to be later in Q4 2024 / early Q1 2025

## SDAC Member Testing

- Simulate real-life trading and EU market coupling
- Planned for February 2025
- Details of the SDAC Member Testing will be provided by SDAC in Autumn 2024


# Summary

- New Go-live date: 18<sup>th</sup> March 2025
- API Package & WSDL: more details will be provided to members at the end of Aug 2024
- Rollback to 60 Minute MTU: SEMOpx members to consider when developing their systems
- Targeted Market Trial: Potentially late Q4 2024 / early Q1 2025
- SDAC Member Testing: Planned for February 2025

# Q & A

## Questions?

Any additional queries, please email us at [info@semopx.com](mailto:info@semopx.com)



Thank You For Attending!
